Croxley Rail Link
RFA Inidicative Headline Programme

ID	Task Name	Duration	Start	Finish
1	**Croxley Rail Link Project (8700)**	**411.2 wks**	**Mon 01/02/10**	**Mon 18/12/17**
2	LUL financial Authority	2 wks	Mon 01/02/10	Fri 12/02/10
3	HCC Cabinet Approval for Scheme Development	1 wk	Mon 15/02/10	Fri 19/02/10
4	Programme Entry	1 day	Mon 22/02/10	Mon 22/02/10
5	**TWA Process**	**94.4 wks**	**Mon 22/02/10**	**Tue 13/12/11**
6	HCC Request for authority to promote Order	1 day	Mon 22/02/10	Mon 22/02/10
7	Development of Scheme for TWA Application	26 wks	Tue 23/02/10	Mon 23/08/10
8	Environmental Appraisal	20 wks	Mon 22/02/10	Fri 09/07/10
9	Pre Application Consultations	16 wks	Mon 31/05/10	Fri 17/09/10
10	Preparation of Draft Order	8 wks	Mon 23/08/10	Fri 15/10/10
11	TWA Application submitted	1 day	Mon 18/10/10	Mon 18/10/10
12	Secretary of State Considers Application	4 wks	Tue 19/10/10	Mon 15/11/10
13	Public Inquiry Preparation / Objection Management	16 wks	Tue 16/11/10	Mon 07/03/11
14	Public Inquiry	4 wks	Tue 08/03/11	Mon 04/04/11
15	Inspector Prepares Report	20 wks	Tue 05/04/11	Mon 22/08/11
16	Secretary of State Considers Report	16 wks	Tue 23/08/11	Mon 12/12/11
17	Secretary of State Decision	1 day	Tue 13/12/11	Tue 13/12/11
18	**Procurement Process**	**208.6 wks**	**Wed 14/12/11**	**Fri 11/12/15**
19	Joint Delivery Agreement Development (JDA)	52 wks	Wed 14/12/11	Tue 11/12/12
20	JDA Signed	1 day	Wed 12/12/12	Wed 12/12/12
21	Design / Procurement Process	78 wks	Thu 13/12/12	Wed 11/06/14
22	Phase 1 Contract Award	1 day	Thu 12/06/14	Thu 12/06/14
23	ECI Phase 1	78 wks	Fri 13/06/14	Thu 10/12/15
24	Phase 2 Contract Award	1 day	Fri 11/12/15	Fri 11/12/15
25	**Construction Activity**	**101.2 wks**	**Mon 11/01/16**	**Mon 18/12/17**
26	Mobilisation	12 wks	Mon 11/01/16	Fri 01/04/16
27	ECI Phase 2 Civils Construction	78 wks	Mon 04/04/16	Fri 29/09/17
28	Rail Elements Construction	32 wks	Mon 27/03/17	Fri 03/11/17
29	Commissioning	6 wks	Mon 06/11/17	Fri 15/12/17
30	Practical Completion / Hand-Over / Line Open	1 day	Mon 18/12/17	Mon 18/12/17

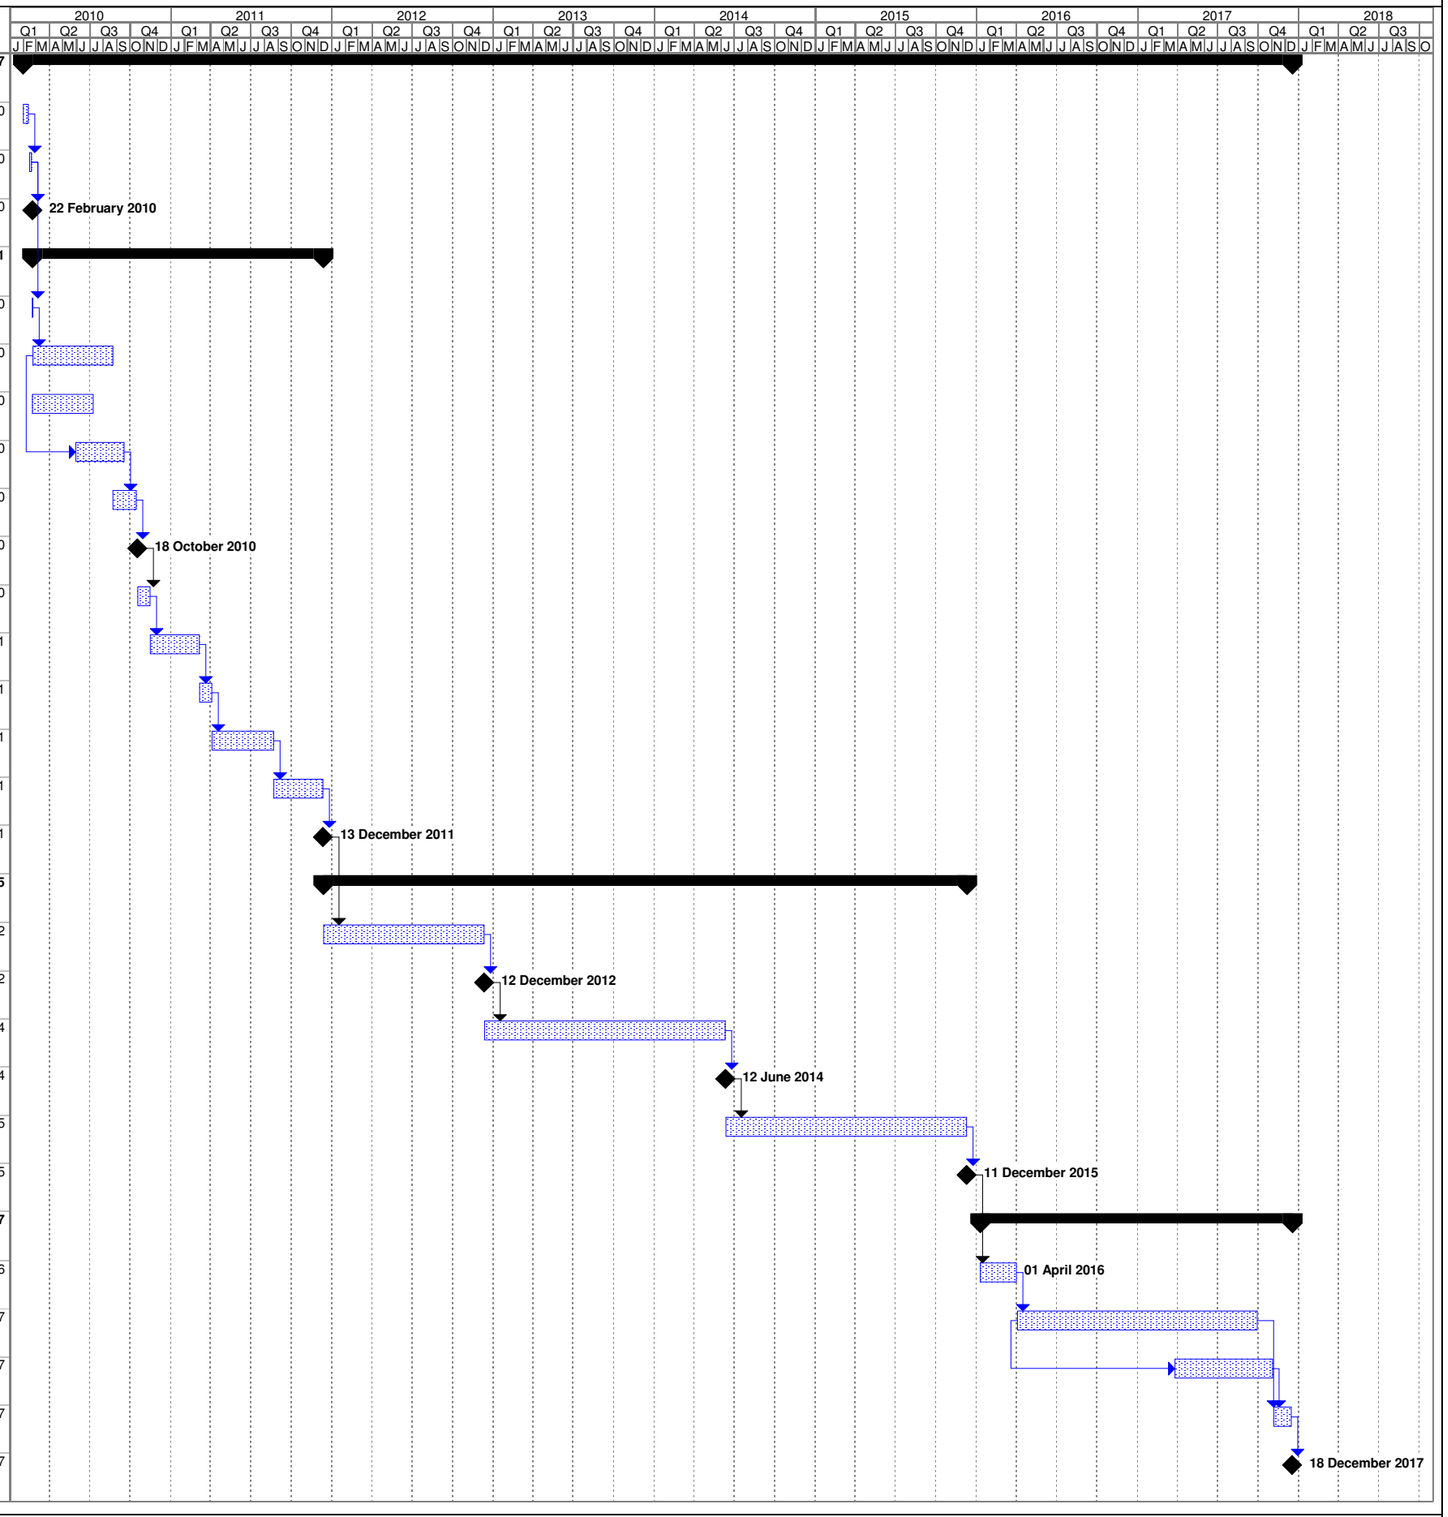

Project: CRL Crit Prog RFA V1
Date: Thu 22/10/09

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | Group By Summary | Deadline
